


Name of the Project: SASEC Road Connectivity Project: Improvement of Joydevpur Chandra-Tangail-Elenga Road (N-4) to a 4-lane Highway.

Name of the Project	:	SASEC Road Connectivity Project: Improvement of Joydevpur Chandra-Tangail-Elenga Road (N-4) to a 4-lane Highway.														
Project Director's Information		Name: Md. Ishaque ID No. 006002 Project Director (ACE, Grade-2), RHD Mobile: 01730-354226														
Location of the Project		Dhaka, Gazipur and Tangail														
Objectives of the Project		<ul style="list-style-type: none"> ◆ Upgrading of existing 70 km Joydevpur-Chandra-Tangail-Elenga (JCTE) 2 Lane Road to 4 Lane Highway ◆ Construction of 9 Flyovers/Overpass, 53 Bridges and 76 Culverts ◆ Construction of separate lane for slow moving vehicles along the JCTE Road ◆ Identification of accident prone locations along JCTE Road and improvement in line with road safety ◆ Construction of RHD Headquarters Building at Tejgaon, Dhaka 														
Implementing Offices		Roads and Highways Department (RHD), Road Transport and Highways Division, Ministry of Road Transport and Bridges														
Main components of the Projects		<table style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 70%;">a) Length of the Road</td> <td style="width: 30%;">70Km</td> </tr> <tr> <td>b) Bridges</td> <td>53 No</td> </tr> <tr> <td>c) Flyover</td> <td>7 No</td> </tr> <tr> <td>d) Railway Overpass</td> <td>2 No</td> </tr> <tr> <td>e) Steel Foot over bridges</td> <td>26 No</td> </tr> <tr> <td>f) Box Culvert</td> <td>76 No</td> </tr> <tr> <td>g) Underpass</td> <td>11 No</td> </tr> </table>	a) Length of the Road	70Km	b) Bridges	53 No	c) Flyover	7 No	d) Railway Overpass	2 No	e) Steel Foot over bridges	26 No	f) Box Culvert	76 No	g) Underpass	11 No
a) Length of the Road	70Km															
b) Bridges	53 No															
c) Flyover	7 No															
d) Railway Overpass	2 No															
e) Steel Foot over bridges	26 No															
f) Box Culvert	76 No															
g) Underpass	11 No															

Project Duration	Approved		Expected		
	April 2013 To June 2020		April 2013 To December 2022		
Project Approval Status	Approval Status	Cost			Duration
		Total	GoB	PA	
	Original	278845.55 Lac	94477.34	184368.21	April 2013- March 2018
	1 st Revised	306680.23 Lac	122312.02	184368.21	April 2013- March 2018
	Special Revised	336474.95 Lac	152106.74	184368.21	April 2013- March 2018
	2 nd Revised	559315.88 Lac	217253.02	342062.86	April 2013- June 2020
	Special Revision (2 nd)	621441.22Lac	279378.36	342062.86	April 2013- June 2022
3 rd Revised	616846.09 Lac	296346.09	320500.00	April 2013- December 2022	
Source of Fund	Asian Development Bank (ADB), OPEC Fund for International Development (OFID) and Abu Dhabi Fund for Development (ADFD)				
Year Wise Financial Information	Year	RDPP Cost Phasing (lac BDT)	ADP/RADP Allocation (Lac BDT)	Expenditure (lac BDT)	
	2012-13	-	-	-	
	2013-14	17821.13	17821.13	17820.94	
	2014-15	15703.45	15703.45	15703.45	
	2015-16	58999.98	58999.98	58999.98	
	2016-17	62015.99	62015.99	62015.99	
	2017-18	86977.50	86977.50	86977.50	
	2018-19	105,000.00	105,000.00	105,000.00	
	2019-20	89929.97	89929.97	89929.97	
	2020-21	61,827.84	61,827.84	61,827.84	
2021-22	91,000.00	67000.00	67000.00		
2022-23	27570.23	51500.00	10254.19		
Present Progress (575,529.54) Lac till August 2022)	Major Components	Quantity & Unit	Progress (%)	Financial (%)	
	a) Length of the Road	70km 4-lane Highway	Physical work of 70 km road widening, Construction of 53 Bridges, 7 Flyovers, 2 Railway Overpass, 11 Underpass and 76 Box culverts is in completed. Physical progress of project is 100.00%.	93.30%	
	b) Bridges	53			
	c) Flyover	7			
	d) Railway Overpass	2			
	e) Steel foot over bridges	26			
f) Box Culvert	76				
Construction Packages	<ul style="list-style-type: none"> ▪ Road Improvement Package -4 nos. ▪ RHD Headquarter Building Construction Package-1no. 				
Location Map					

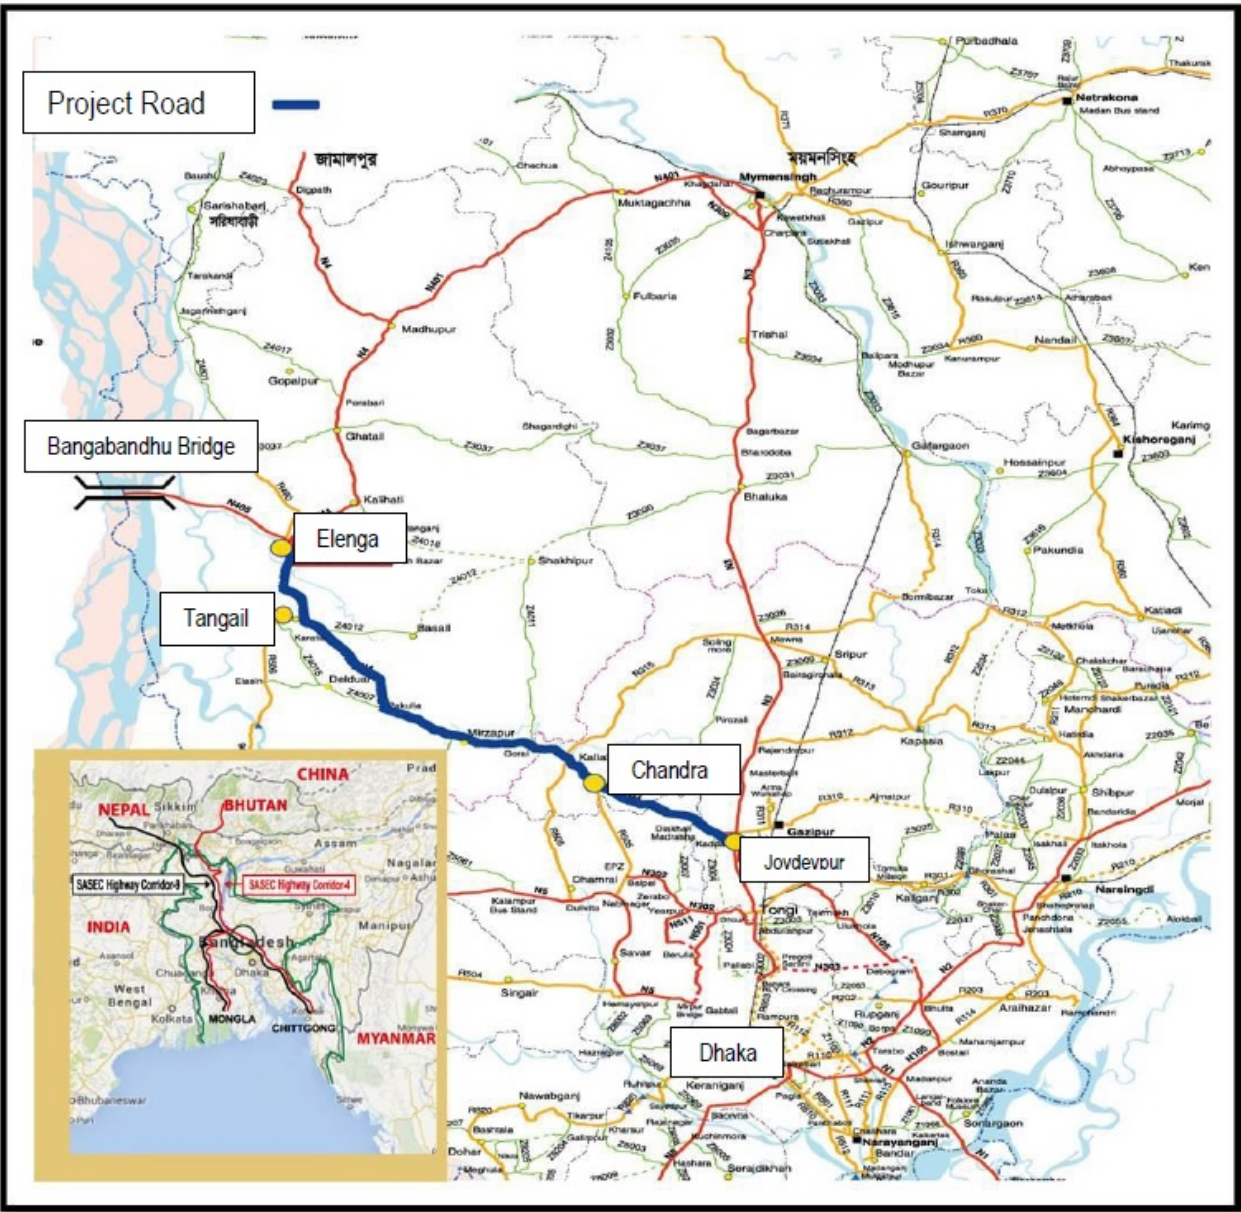

Project Road

Bangabandhu Bridge

Elega

Tangail

Chandra

Jovdevour

Dhaka

